




METALWORKS® ESTIMATE SHEET

JOB NAME _____ DATE _____
 ADDRESS: _____ PHONE # _____

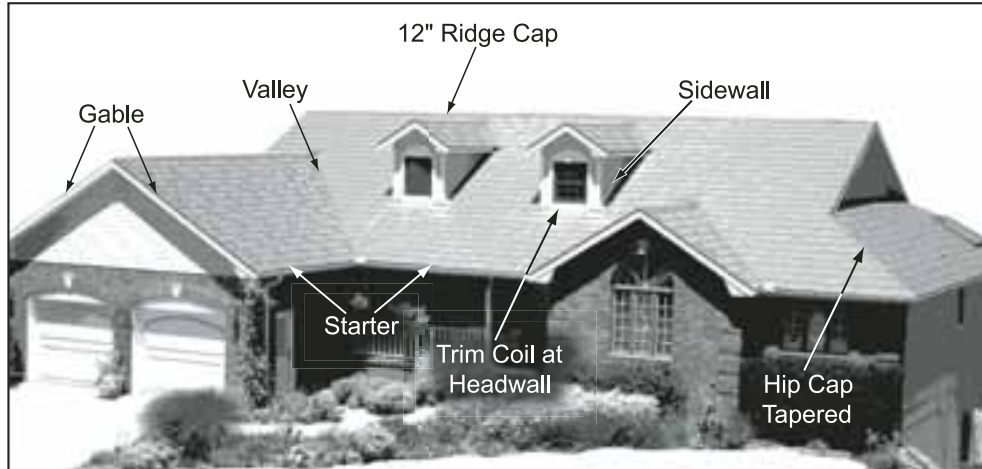

STONECREST™ SLATE

- Sequoia Red
- Sierra Slate Grey
- Vermont Blue
- Quaker Green

STONECREST™ TILE

- Sierra Slate Grey
- Vermont Blue
- Quaker Green

ASTONWOOD™

- River Rock Brown
- Timber Brown
- Forest Green
- Sequoia Red
- Vermont Blue
- Sierra Slate Grey
- Brite Red

SHINGLES

Roof Areas Measured in Feet:

_____ X _____	= _____		sqft
_____ X _____	= _____		sqft
_____ X _____	= _____		sqft
_____ X _____	= _____		sqft
_____ X _____	= _____		sqft
_____ X _____	= _____		sqft
_____ X _____	= _____		sqft
TOTAL ROOF AREA = _____			sqft

TRIM COMPONENTS

Starter	_____ ft	Ridge	_____ ft
Gable	_____ ft	Hip	_____ ft
Headwall	_____ ft	Sidewall	_____ ft
Valley	_____ ft	J Channel	_____ ft

TOTAL SHINGLE CARTONS

AstonWood _____ sqft div by 100 = _____ total ctns
 StoneCrest Slate _____ sqft div by 50 = _____ total ctns
 StoneCrest Tile _____ sqft div by 50 = _____ total ctns

SHINGLE COST

Total Shingle ctns _____ X \$ _____ per ctn = \$ _____

(Figure your waste factor for all calculations)



TRIM COMPONENTS

STARTER/ EAVE

10 pcs/ctn 10 ft. length

Eave Edge

Total Eave Length _____ ÷ 10ft = _____ pcs X \$ _____ per pc = \$ _____ cost




GABLE/ RAKE

10 pcs/ctn 10 ft. length

Rake Edge

Total Gable Length _____ ÷ 10ft = _____ pcs X \$ _____ per pc = \$ _____ cost




12 inch RIDGE CAP

25 pcs/ctn 25 lineal ft.

Ridge Cap

Total Ridge Length _____ ÷ 25ft = _____ ctns X \$ _____ per ctn = \$ _____ cost



HIP CAP TAPERED


50 pcs/ctn 50 lineal ft.

AstonWood Hip Cap

Total Ridge Length _____ ÷ 50ft = _____ ctns X \$ _____ per ctn = \$ _____ cost

StoneCrest Hip Cap


Total Ridge Length _____ ÷ 50ft = _____ ctns X \$ _____ per ctn = \$ _____ cost



TRIM COIL

22-1/4" X 50'

_____ ctns \$ _____ cost



SIDEWALL

5 pcs/ctn 10 ft. length


Total Sidewall Length _____ ÷ 10ft = _____ pcs X \$ _____ per pc = \$ _____ cost



VALLEY

5 Pcs/ctn 10 ft. length

Total Valley Length _____ ÷ 10ft = _____ pcs X \$ _____ per pc = \$ _____ cost



J CHANNEL

10 pcs/ctn 10 ft. length

Total J Channel Length _____ ÷ 10ft = _____ pcs X \$ _____ per pc = \$ _____ cost



ACCESSORIES

CLIPS

400 clips per ctn (+/- 100 clips per square) _____ ctns X \$ _____ per ctn = \$ _____ cost



SCREWS

50 screws per bag _____ bags X \$ _____ per bag = \$ _____ cost



SNOW GUARDS

100 snow guards/ctn _____ ctns X \$ _____ per ctn = \$ _____ cost



HIP & RIDGE SEAL

4" X 50' _____ rolls X \$ _____ per roll = \$ _____ cost



TOUCH-UP PAINT

2 oz. bottle _____ btls X \$ _____ per btl = \$ _____ cost



TW METAL AND TILE UNDERLAYMENT 2 sq. roll _____ rolls X \$ _____ roll = \$ _____ cost

No. 30 FELT 2 sq. roll _____ rolls X \$ _____ roll = \$ _____ cost

RAPID RIDGE 20 ft. roll 50 ft. roll _____ rolls X \$ _____ roll = \$ _____ cost

TOTAL TAMKO MATERIAL COST \$ _____

This sheet is provided by TAMKO for convenience purposes only and the user is solely responsible for all calculations and estimates associated with the use hereof. TAMKO expressly disclaims any and all liabilities associated with the use of this sheet or the information provided herein.
